Activity ID	Activity Name	Original Duration	Remaining Duration	Duration % Complete	Start	Finish
7642 Fresno USD Program Schedule MAY 2026 UD v2026.06.		4860	2938	39.55%	01-Feb-25 A	20-Jun-34
FUSD-DMSCP-2000	MEASURE H BOND PROGRAM MANAGEMENT	365	105	71.23%	01-Jul-25 A	17-Sep-26
FUSD.FRSNO.1005	MEASURE H PROGRAM MANAGEMENT	366	106	71.04%	01-Jul-25 A	18-Sep-26
MILESTONE		0	0	0%	01-Feb-25 A	01-Feb-25 A
FRESNO.USD.0001	NTP Measure H Bond	0	0	100%	01-Feb-25 A	
PROCUREMENT of BOND ISSUANCE		2443	2218	9.21%	01-Feb-25 A	30-Jun-32
FUSD.BOND.1010	Procurement of Issuance A	182	0	100%	01-Feb-25 A	01-Aug-25 A
FUSD.BOND.1020	Procurement of Issuance B	121	22	81.82%	01-Feb-26 A	26-Jun-26
FUSD.BOND.1030	Procurement of Issuance C	150	150	0%	01-Feb-27*	30-Jun-27
FUSD.BOND.1040	Procurement of Issuance D	151	151	0%	01-Feb-28*	30-Jun-28
FUSD.BOND.1050	Procurement of Issuance E	150	150	0%	01-Feb-29*	30-Jun-29
FUSD.BOND.1060	Procurement of Issuance F	150	150	0%	01-Feb-30*	30-Jun-30
FUSD.BOND.1070	Procurement of Issuance G	150	150	0%	01-Feb-31*	30-Jun-31
FUSD.BOND.1080	Procurement of Issuance H	151	151	0%	01-Feb-32*	30-Jun-32
Farber South (Measure M Carry-over)					16-Jun-25 A	
Farber South Building B Replace (On Hold)					16-Jun-25 A	
Preconstruction					16-Jun-25 A	
Construction						
Fresno HS- Phase 1 (Measure M Carry-over)		1350	515	61.85%	01-Feb-25 A	01-Nov-27
Fresno High Cafeteria		844	515	38.98%	05-Mar-25 A	01-Nov-27
Preconstruction		71	0	100%	05-Mar-25 A	18-Jun-25 A
Construction		769	515	33.03%	01-Jul-25 A	01-Nov-27
Maintenance Shed/PC		987	447	54.71%	01-Feb-25 A	25-Aug-27
Preconstruction		594	13	97.81%	01-Feb-25 A	17-Jun-26
Construction		423	423	0%	29-Jun-26	25-Aug-27
Hoover HS (Measure M Carry-over)		1280	880	31.25%	01-May-25 A	31-Oct-28
Hoover Admin Building Replacement		1280	880	31.25%	01-May-25 A	31-Oct-28
Preconstruction		848	448	47.17%	01-May-25 A	26-Aug-27
Construction		427	427	0%	01-Sep-27	31-Oct-28
Roosevelt HS- Phase 1 (Measure M Carry-over)		1310	880	32.82%	01-Apr-25 A	31-Oct-28
H403 - Roosevelt Admin Building Replacement		1310	880	32.82%	01-Apr-25 A	31-Oct-28
Preconstruction		878	448	48.97%	01-Apr-25 A	26-Aug-27
Construction		429	429	0%	30-Aug-27	31-Oct-28
Norseman EL Classroom Master Plan		1704	1252	26.53%	10-Mar-25 A	07-Nov-29
Preconstruction		1174	722	38.5%	10-Mar-25 A	26-May-28
Construction		530	530	0%	27-May-28	07-Nov-29
Birney EL Classroom & MPR Master Plan		1707	1255	26.48%	10-Mar-25 A	10-Nov-29
Preconstruction		1177	725	38.4%	10-Mar-25 A	29-May-28
Construction		530	530	0%	30-May-28	10-Nov-29
Del Mar Portable Replacement Master Plan		1759	1307	25.7%	10-Mar-25 A	01-Jan-30
Preconstruction		1159	707	39%	10-Mar-25 A	11-May-28
Construction		600	600	0%	12-May-28	01-Jan-30
Calwa EL Building Master Plan		1732	1280	26.1%	10-Mar-25 A	05-Dec-29
Preconstruction		1202	750	37.6%	10-Mar-25 A	23-Jun-28
Construction		530	530	0%	24-Jun-28	05-Dec-29
Ericson Portable Replacement Master Plan		1790	1338	25.25%	10-Mar-25 A	01-Feb-30
Preconstruction		1190	738	37.98%	10-Mar-25 A	11-Jun-28
Construction		600	600	0%	12-Jun-28	01-Feb-30

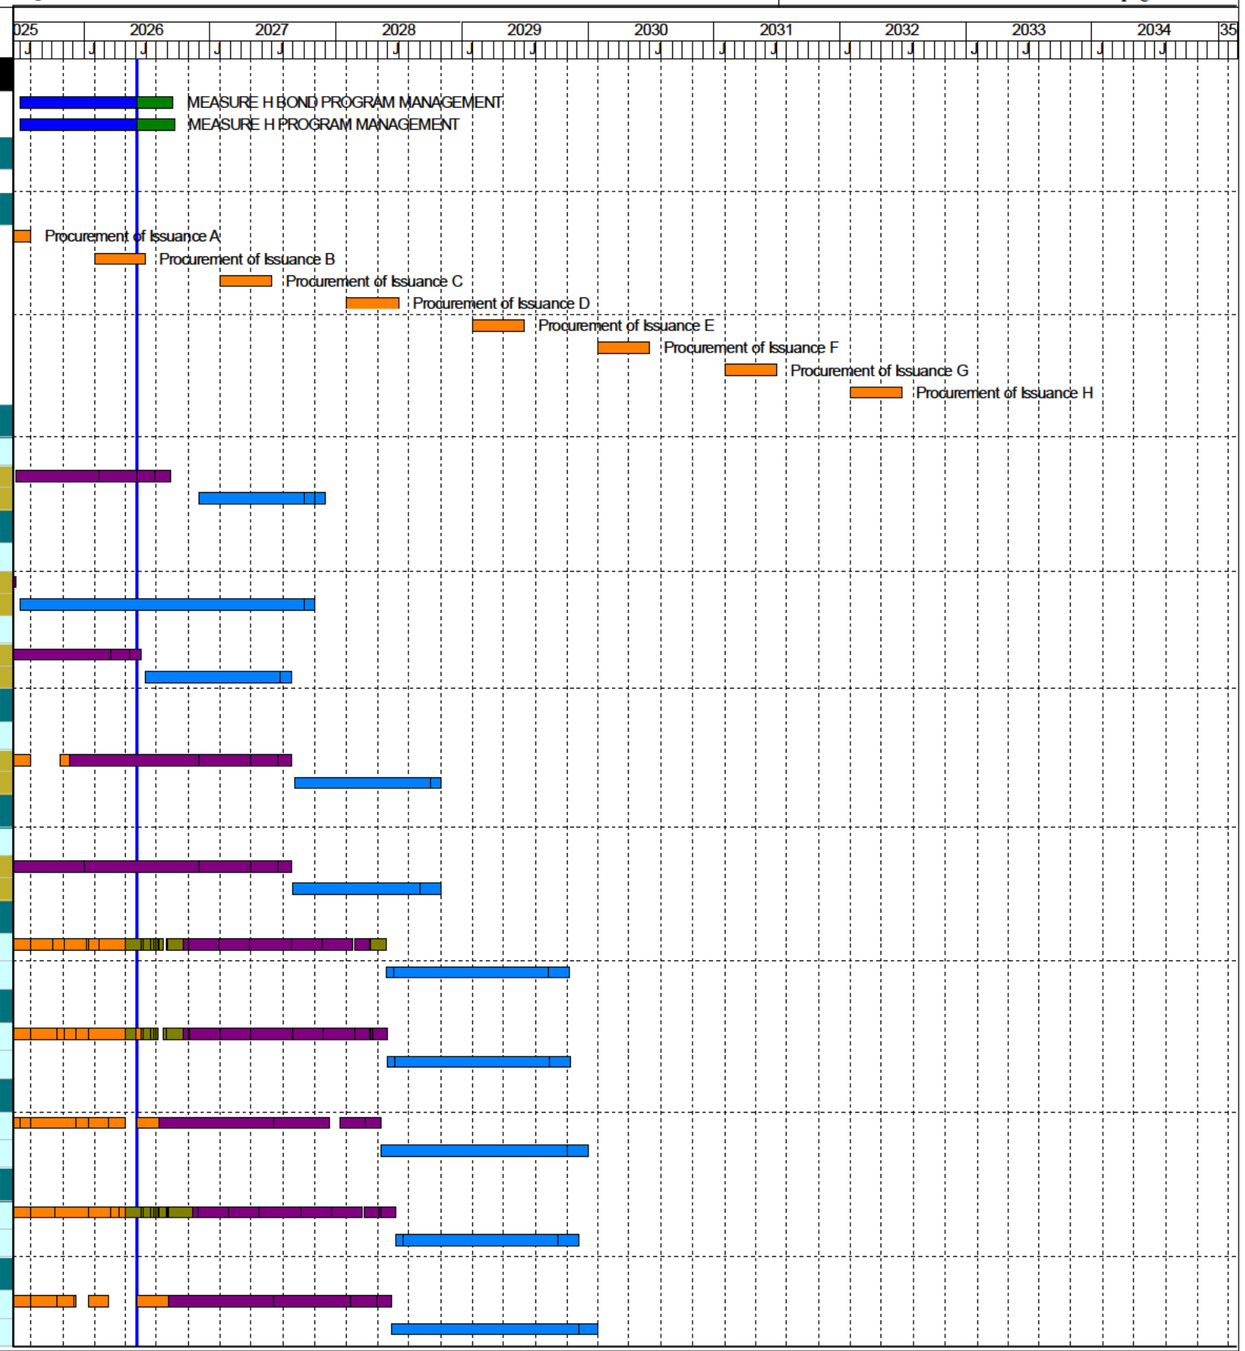

Data Date: **05-Jun-26**
Run Date: 08-Jun-26
Layout: -FRESNO PROGRAM PRIORITY-SUMMARY
Filters: TASK filters: No Costs, No Measure M- Prior Feb 2025.

Remaining Work
Actual Work
MASTER
RFP
DESIGN & BID
CONSTRUCTION

Measure 'H' Project Schedule – Working File
Subject to Change – File Will be Routinely Updated

PRIORITY PROJECTS

Fresno Unified School District

KITCHELL

Activity ID	Activity Name	Original Duration	Remaining Duration	Duration % Complete	Start	Finish
	Addams Portable Replacement Master Plan	1736	1284	26.04%	10-Mar-25 A	09-Dec-29
	Preconstruction	1136	684	39.79%	10-Mar-25 A	18-Apr-28
	Construction	600	600	0%	19-Apr-28	09-Dec-29
	King Portable Replacement	1276	1270	0.47%	01-Apr-26 A	25-Nov-29
	Preconstruction	706	700	0.85%	01-Apr-26 A	04-May-28
	Construction	570	570	0%	05-May-28	25-Nov-29
	Lane Admin Relocation	1473	1473	0%	10-Sep-26	21-Sep-30
	Preconstruction	903	903	0%	10-Sep-26	28-Feb-29
	Construction	570	570	0%	01-Mar-29	21-Sep-30
	Centennial Cafeteria Reconstruction	1582	1582	0%	23-Jan-27	23-May-31
	Preconstruction	1002	1002	0%	23-Jan-27	20-Oct-29
	Construction	580	580	0%	21-Oct-29	23-May-31
	Viking Restrooms ADA Compliant	956	956	0%	09-May-28	20-Dec-30
	Preconstruction	681	681	0%	09-May-28	20-Mar-30
	Construction	275	275	0%	21-Mar-30	20-Dec-30
	Bullard Talent Theatre Improv & Fire Safety	973	973	0%	13-Sep-28	13-May-31
	Preconstruction	578	578	0%	13-Sep-28	13-Apr-30
	Construction	395	395	0%	14-Apr-30	13-May-31
	Pyle Portable Replacement	1612	1612	0%	24-May-27	21-Oct-31
	Preconstruction	1002	1002	0%	24-May-27	18-Feb-30
	Construction	610	610	0%	19-Feb-30	21-Oct-31
	Jefferson Restrooms ADA Compliant	956	956	0%	02-Jan-28	14-Aug-30
	Preconstruction	681	681	0%	02-Jan-28	12-Nov-29
	Construction	275	275	0%	13-Nov-29	14-Aug-30
	Roeding Restroom ADA Compliant	956	956	0%	01-Feb-28	13-Sep-30
	Preconstruction	681	681	0%	01-Feb-28	12-Dec-29
	Construction	275	275	0%	13-Dec-29	13-Sep-30
	Roosevelt Turf, Track, Lights & Stands/Roosevelt HS- F	2550	2550	0%	01-Jul-26	23-Jun-33
	Preconstruction	1970	1970	0%	01-Jul-26	21-Nov-31
	Construction	580	580	0%	22-Nov-31	23-Jun-33
	Yosemite Partial Renovations	1612	1612	0%	16-Apr-28	13-Sep-32
	Preconstruction	1002	1002	0%	16-Apr-28	12-Jan-31
	Construction	610	610	0%	13-Jan-31	13-Sep-32
	Wolters Portable Replacement	1434	1434	0%	13-Mar-29	13-Feb-33
	Preconstruction	864	864	0%	13-Mar-29	24-Jul-31
	Construction	570	570	0%	25-Jul-31	13-Feb-33
	Fort Miller Partial Renovations	1612	1612	0%	20-Jun-28	17-Nov-32
	Preconstruction	1002	1002	0%	20-Jun-28	18-Mar-31
	Construction	610	610	0%	19-Mar-31	17-Nov-32
	Kratt Restroom and ADA Compliant	956	956	0%	04-Aug-28	17-Mar-31
	Preconstruction	681	681	0%	04-Aug-28	15-Jun-30
	Construction	275	275	0%	16-Jun-30	17-Mar-31
	Leavenworth GN Restroom ADA Compliant	956	956	0%	04-Aug-29	16-Mar-32
	Preconstruction	681	681	0%	04-Aug-29	15-Jun-31
	Construction	275	275	0%	16-Jun-31	16-Mar-32
	Hidalgo Restroom ADA Compliant	956	956	0%	02-Nov-29	14-Jun-32
	Preconstruction	681	681	0%	02-Nov-29	13-Sep-31
	Construction	275	275	0%	14-Sep-31	14-Jun-32

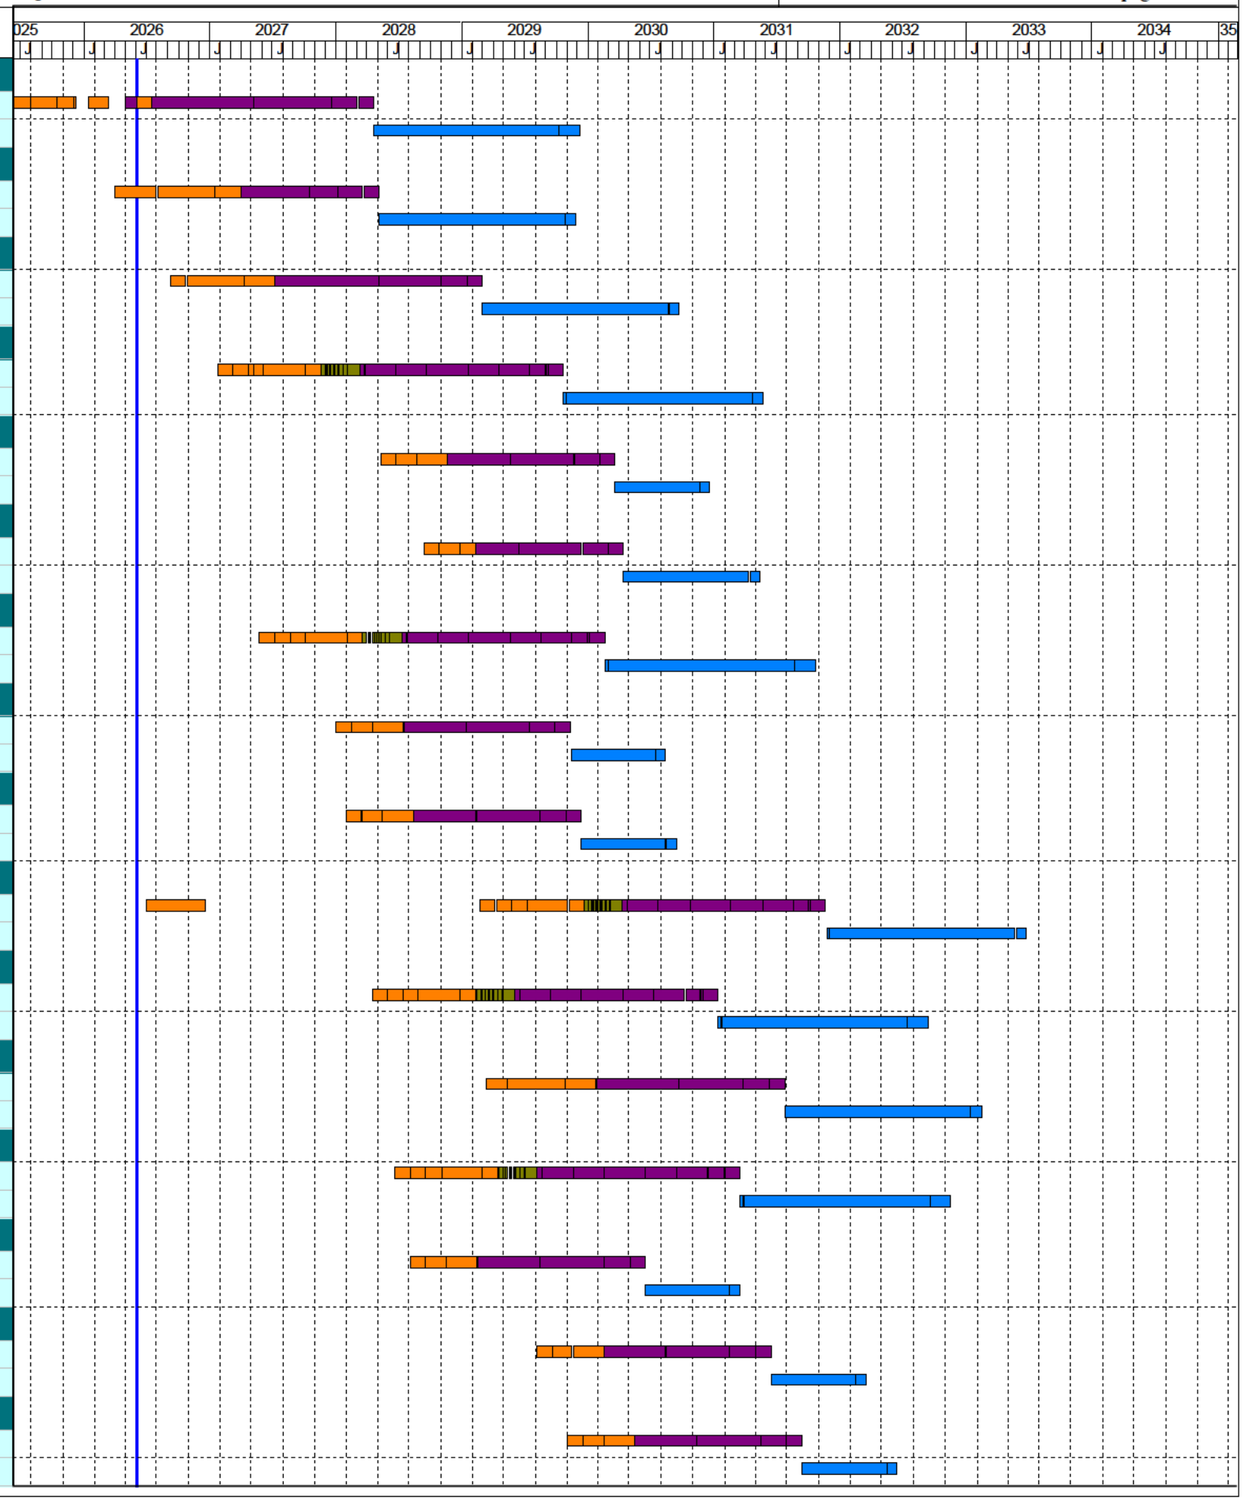
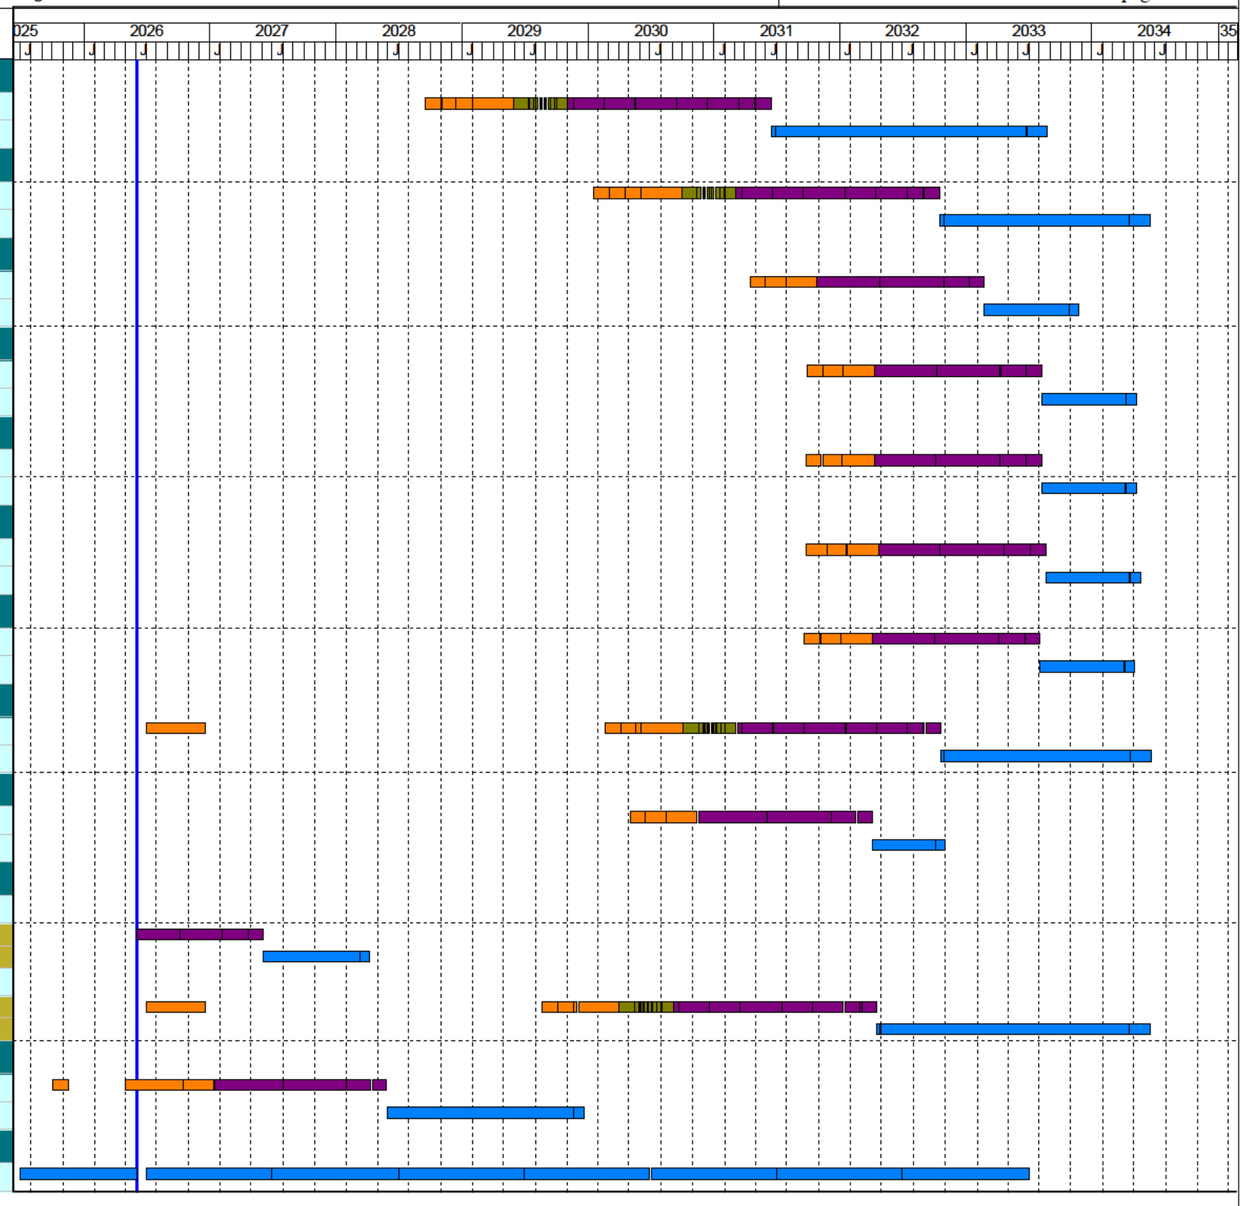
Activity ID	Activity Name	Original Duration	Remaining Duration	Duration % Complete	Start	Finish
	Kirk Partial Renovations	1802	1802	0%	18-Sep-28	24-Aug-33
	Preconstruction	1002	1002	0%	18-Sep-28	16-Jun-31
	Construction	800	800	0%	17-Jun-31	24-Aug-33
	Computech Partial Renovations	1612	1612	0%	19-Jan-30	18-Jun-34
	Preconstruction	1002	1002	0%	19-Jan-30	16-Oct-32
	Construction	610	610	0%	17-Oct-32	18-Jun-34
	Lincoln Restroom ADA Compliance	956	956	0%	15-Apr-31	25-Nov-33
	Preconstruction	681	681	0%	15-Apr-31	23-Feb-33
	Construction	275	275	0%	24-Feb-33	25-Nov-33
	Malloch Restroom ADA Compliant	955	955	0%	28-Sep-31	09-May-34
	Preconstruction	680	680	0%	28-Sep-31	07-Aug-33
	Construction	275	275	0%	08-Aug-33	09-May-34
	Storey Restroom ADA Compliant	956	956	0%	26-Sep-31	08-May-34
	Preconstruction	681	681	0%	26-Sep-31	06-Aug-33
	Construction	275	275	0%	07-Aug-33	08-May-34
	Balderas Restroom ADA Compliant	970	970	0%	24-Sep-31	20-May-34
	Preconstruction	695	695	0%	24-Sep-31	18-Aug-33
	Construction	275	275	0%	19-Aug-33	20-May-34
	Ayer ES Restrooms ADA Compliant	956	956	0%	22-Sep-31	04-May-34
	Preconstruction	681	681	0%	22-Sep-31	02-Aug-33
	Construction	275	275	0%	03-Aug-33	04-May-34
	Fresno High Turf, Track, Lights & Stands/Fresno HS- F	2912	2912	0%	01-Jul-26	20-Jun-34
	Preconstruction	2302	2302	0%	01-Jul-26	18-Oct-32
	Construction	610	610	0%	19-Oct-32	20-Jun-34
	Sunnyside HS	915	915	0%	04-May-30	03-Nov-32
	Preconstruction	701	701	0%	04-May-30	03-Apr-32
	Construction	214	214	0%	04-Apr-32	03-Nov-32
	Bullard Turf, Track, Lights & Stands	2934	2934	0%	05-Jun-26	16-Jun-34
	Phase 1 Restroom & Concessions Building-1	674	674	0%	05-Jun-26	08-Apr-28
	Preconstruction	366	366	0%	05-Jun-26	05-Jun-27
	Construction	308	308	0%	06-Jun-27	08-Apr-28
	Phase 2 Remaining Scope	2908	2908	0%	01-Jul-26	16-Jun-34
	Preconstruction	2118	2118	0%	01-Jul-26	17-Apr-32
	Construction	790	790	0%	18-Apr-32	16-Jun-34
	Sunnyside CTE Ag Farm	1319	1294	1.9%	06-Oct-25 A	19-Dec-29
	Preconstruction	755	724	4.11%	06-Oct-25 A	28-May-28
	Construction	570	570	0%	29-May-28	19-Dec-29
	Deferred Maintenance & Small Capital Projects	2557	2583	0%	01-Jul-25 A	30-Jun-33
	DM & Small Capital	2557	2583	0%	01-Jul-25 A	30-Jun-33
